

Construction Management Report

— June 2021 —

Demolition Package 1C

Parcels 34, 87, 90, 106, 107; Norm West Park restroom facility

- ◆ Marschel Wrecking completed demolition of structures at Parcels 106 and 107 (2820 | 2828 Breckenridge Industrial Ct - Omni | Becker) on June 10.
- ◆ Marschel Wrecking completed abatement work and sewer | water utility disconnects to Parcel 87 (2714 Breckenridge Industrial Ct - Midwest Flooring) on June 17.
- ◆ Marschel Wrecking is currently awaiting electric disconnects and demolition permitting for Parcel 87 (2714 Breckenridge Industrial Ct - Midwest Flooring) for commencing demolition.

Summary

- ◆ Current Contract Cost: \$368,140.00
- ◆ Contract Completion Date: August 30, 2021.
- ◆ Change Orders - None

Flood Mitigation Phase I

- ◆ L.Keeley is currently working on:
 - ◆ 72" sewer line installation near the South end of Bompart Ave.
 - ◆ Installation of large sewer junction chambers at Mary Ave.
 - ◆ Prep work for bypass pumping of the existing horseshoe sewer.
 - ◆ Excavated soils export.
 - ◆ Storm water pollution prevention plan routine maintenance and repairs.

Summary

- ◆ Current Contract Cost: \$17,192,574
- ◆ Contract Completion Date: July 19, 2022
- ◆ Change Orders - None
- ◆ Risks at this Point - Unknown Buried Items, Potential Impacted Soils, Soft Unsatisfactory Subgrade Soils



**Brentwood
Bound**
Building a Bright Future



72" sewer line installation near the South end of Bompat Ave.



Large sewer junction chamber installed at Mary Ave.



**Brentwood
Bound**
Building a Bright Future



24" sewer discharge piping for bypass pumping the existing horseshoe sewer.




Loading and haul off of excavated soils from the 72" sewer line installation.





Demolition of structures at Parcels 106 |107 (2820 | 2828 Breckenridge Industrial Ct - Omni | Becker)

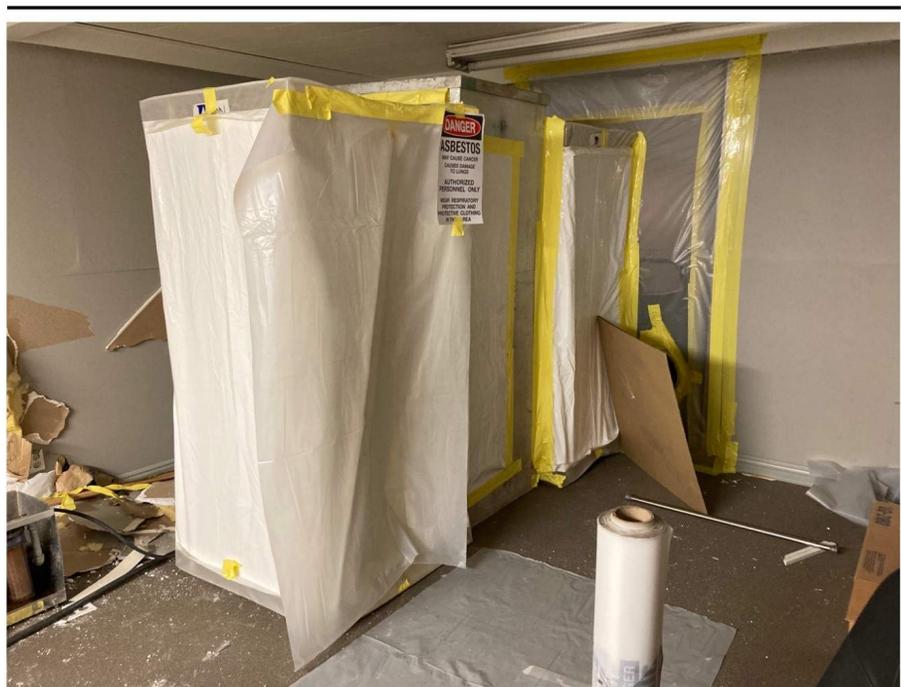

Interior abatement at Parcel 87 (2714 Breckenridge Industrial Ct - Midwest Flooring).
